

CONTRA COSTA COUNTY
DEPARTMENT OF TRANSPORTATION



TO: Kevin Emigh, PE
DIVISION MANAGER
DEPARTMENT OF PUBLIC WORKS

Job Stamp:
Alhambra Valley Road Washout Project
County Project No. 0667-6U6201
Federal Aid Project No. PR ER-32LO()

SUBJECT: WEEKLY NEWSLETTER

WEEK ENDING	<u>November 04, 2017</u>		
%TIME ELAPSED	<u>169.3</u>	% COMPLETE	<u>100.0</u>
EST DATE OF COMPLETION	<u>November 02, 2017</u>		
DATE CONTRACT TIME EXPIRES	<u>September 05, 2017</u>		

THIS PAST WEEK THE FOLLOWING WORK WAS DONE:

Grind and Groove Bridge Deck,
Striping,
Shoulder backing,
Joint Seal,
Erosion Control,
Final Cleanup.

WORK NEXT WEEK WILL PROBABLY CONSIST OF:

NONE: PROECT COMPLETE on 11/02/17

PROJECT ISSUES:

Contractor is behind schedule with no anticipated catch up schedule. Contractor has exceeded working days, however, there are CCO's in process that will extend the date of completion.

A handwritten signature in blue ink, appearing to read 'Ramon Montes de Oca'.

Ramon Montes de Oca, PE
Resident Engineer
Quincy Engineering, Inc.


cc: Slava Gospodchikov, Contra Costa County
Steve Mellon, QEI

Attachment – site photos
Original – File

Weekly Newsletter – Week Ending November 04, 2017
Site Photos



HMA Dike being installed.

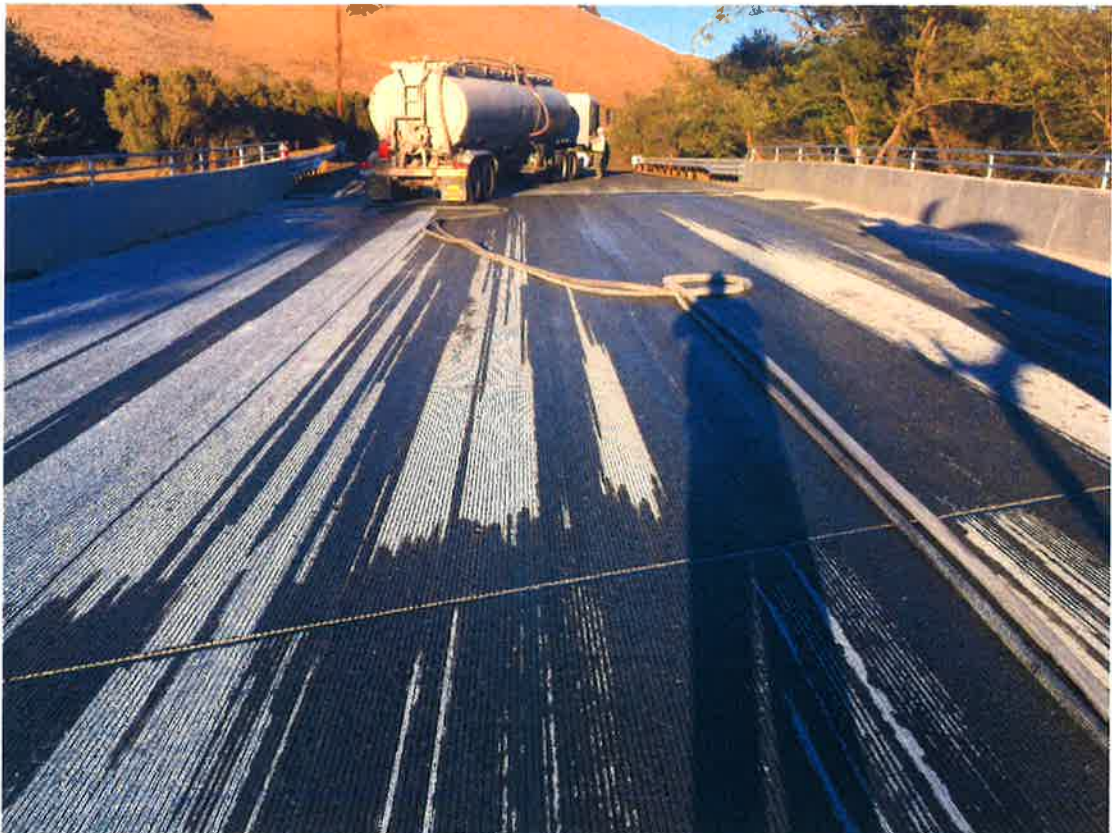

Bridge deck being ground and grooved.

Weekly Newsletter – Week Ending November 04, 2017
Site Photos



Erosion control placed and fiber rolls around drainage inlets.



Project Complete! Road open 11/02/2017.
