County of Contra Costa
2014 Microsurfacing Project No. 0672-6U2151-14
Baseline Schedule

| ID | | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 1 | | Notice of Award | 1 day | Tue 5/27/14 | Tue 5/27/14 |
| 2 | | Preconstruction Meeting | 1 day | Mon 6/2/14 | Mon 6/2/14 |
| 3 | | Submittal Review | 10 days | Tue 6/3/14 | Mon 6/16/14 |
| 4 | | **Notice to Proceed** | **45 days** | **Mon 6/16/14** | **Fri 8/15/14** |
| 5 | | Construction Area Signs | 3 days | Mon 6/16/14 | Wed 6/18/14 |
| 6 | | USA Digouts | 2 days | Thu 6/19/14 | Fri 6/20/14 |
| 7 | | Digout Notification | 2 days | Thu 6/19/14 | Fri 6/20/14 |
| 8 | | Digout Area 1 Danville Blvd | 2 days | Mon 6/23/14 | Tue 6/24/14 |
| 9 | | Digout Area 2 Treat Blvd | 1 day | Wed 6/25/14 | Wed 6/25/14 |
| 10 | | Digout Area 3 Kensington | 3 days | Thu 6/26/14 | Mon 6/30/14 |
| 11 | | Install Loops | 1 day | Thu 6/26/14 | Thu 6/26/14 |
| 12 | | Notify Micro Surfacing | 1 day | Wed 7/9/14 | Wed 7/9/14 |
| 13 | | Micro Surface Prep Work | 4 days | Thu 7/10/14 | Tue 7/15/14 |
| 14 | | Striping Removal | 4 days | Wed 7/16/14 | Mon 7/21/14 |
| 15 | | Micro Surfacing Area 1 Treat Blvd | 3 days | Thu 7/17/14 | Mon 7/21/14 |
| 16 | | Micro Surfacing Area 2 Danville Blvd | 4 days | Wed 7/23/14 | Mon 7/28/14 |
| 17 | | Micro Surfacing Area 3 Richmond Parkway | 1 day | Tue 7/29/14 | Tue 7/29/14 |
| 18 | | Micro Surfacing Area 4 Kensington | 4 days | Wed 7/30/14 | Mon 8/4/14 |
| 19 | | Striping Installation | 10 days | Tue 7/29/14 | Mon 8/11/14 |
| 20 | | Final Clean Up | 2 days | Tue 8/12/14 | Wed 8/13/14 |
| 21 | | Project Complete (NTP + 45 WK DA) | 0 days | Wed 8/13/14 | Wed 8/13/14 |

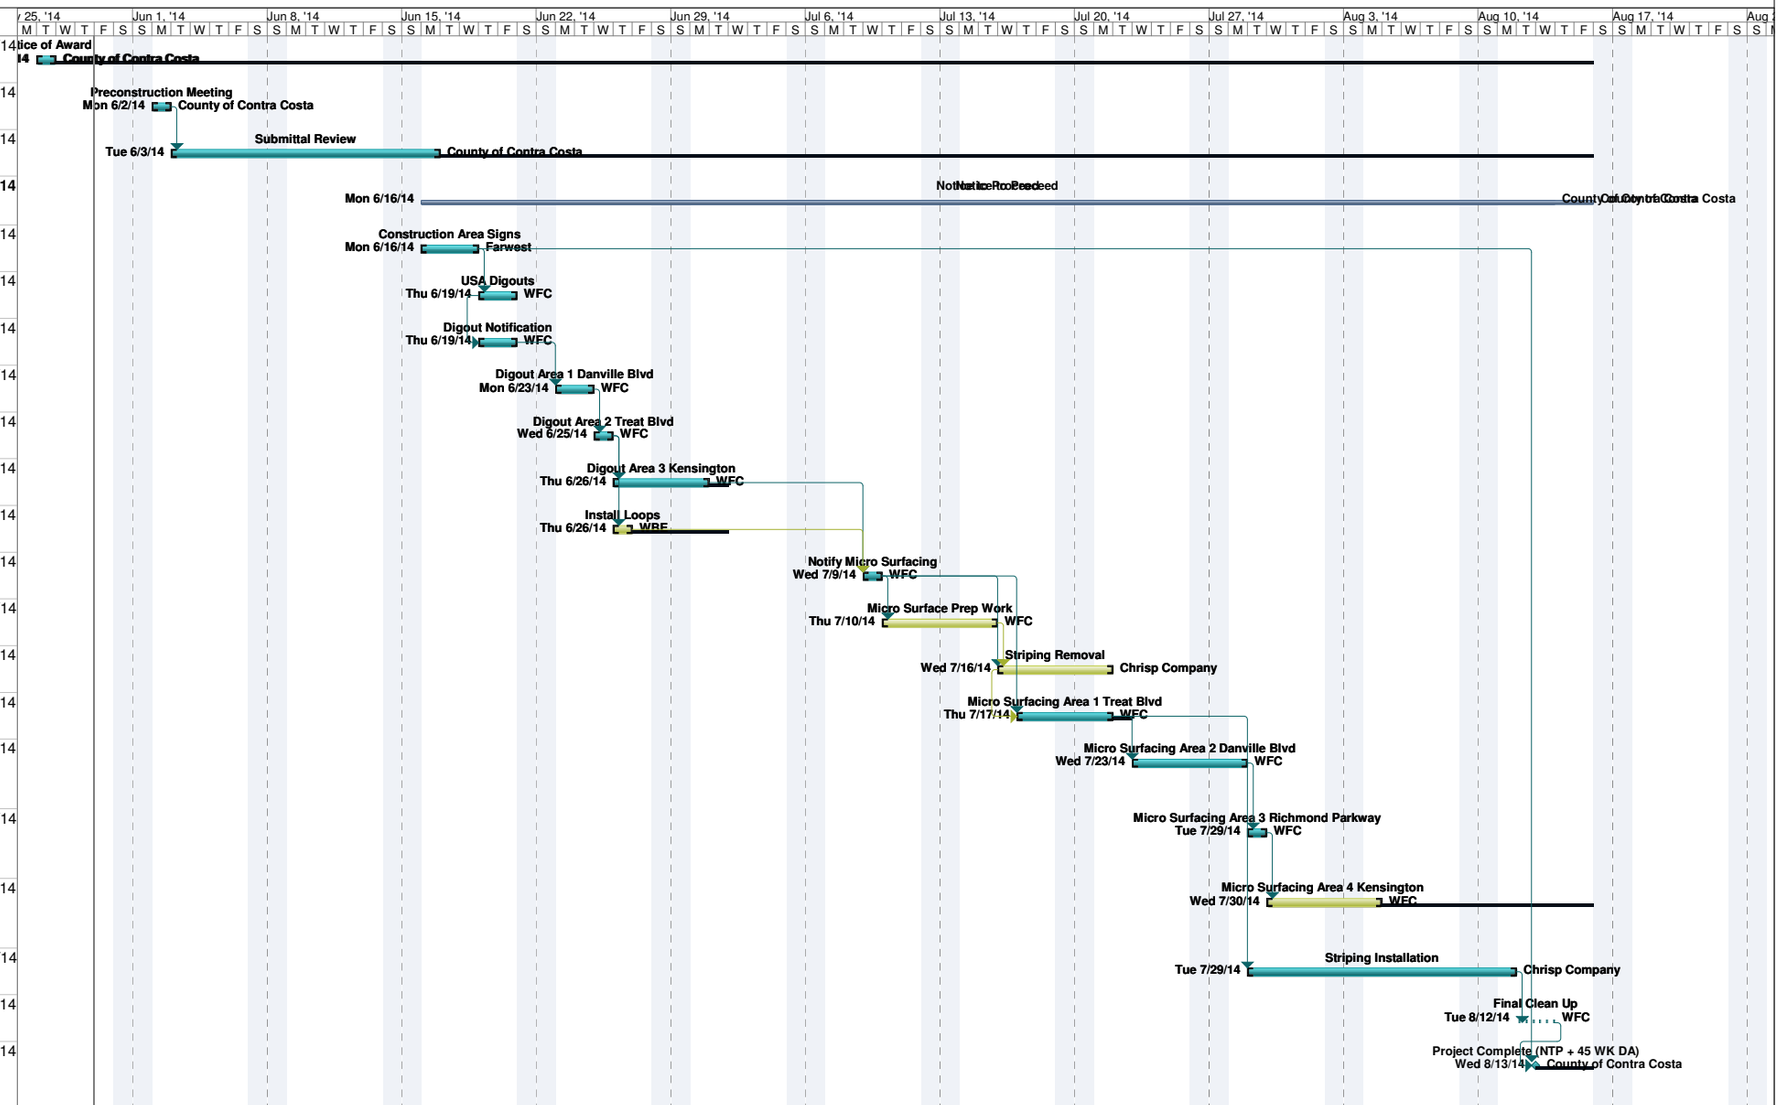


Project: 146006 Contra Costa County
Date: Fri 5/30/14

| | | | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|
| Task | | Project Summary | | Inactive Task | | Duration-only | | Finish-only | | Progress | |
| Split | | External Tasks | | Inactive Milestone | | Manual Summary Rollup | | Baseline | | Deadline | |
| Milestone | | External Milestone | | Inactive Summary | | Manual Summary | | Baseline Milestone | | Slack | |
| Summary | | Inactive Task | | Manual Task | | Start-only | | Baseline Summary | | | |
